June 28, 2013

Current Response Status/Activities

Neighborhood

- Have completed hydro-vacing around utilities between #20 and #24
- Covering excavation along driveway of #50 have contacted fence contractor
- Awaiting sample results from #50

Main Street

• No change - continue monitoring and maintenance activities

365

 Have completed hydro-vacing small area near 365 along creek where small amount of oil was found

Cove

- Continue monitoring and maintenance, including airboat pom-pom operations
- Working to finalize boom removal strategy replacing skirt boom south of willows

Attachments

- Northwoods Air Sampling Results/Meetings with Homeowners
- Northwoods Excavation Plan/Update

MDW 06/27/13

June 28, 2013

Key Incident Statistics

Solid Waste Summary (original response)

	Soil	Debris	Wood Chips	Vac Boxes	Total
Conway	0	1	0	0	1
Landfill	433	315	281	79	1108
Total	433	316	281	79	1109

Have generated additional roll offs from maintenance activities (hydro vacuuming)

Solid Waste Summary (recent residential remediation)

	Soil	Debris	Wood Chips	Vac Boxes	Total
(EMES)	25	0	0	0	25
Landfill	11	0	0	0	11
Left	16	0	0	0	16

Awaiting sample results prior to disposal

Oil/Liquids Summary (number of fracs)


	Total Fracs	Fracs Shipped	Fracs Left
Oil/water to Rineco	26	26	0
Decon water to Rineco	8	8	0
Oil/water to BRRF	38	38	0
Total oil/water	72	72	0

Note: 37 drums of decon water bottoms have been sent to Rineco


June 28, 2013

Northwoods Subdivision

Updated: 6/27/13

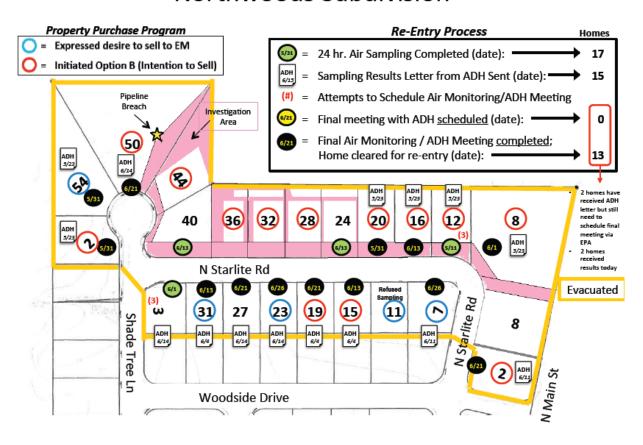

June 28, 2013

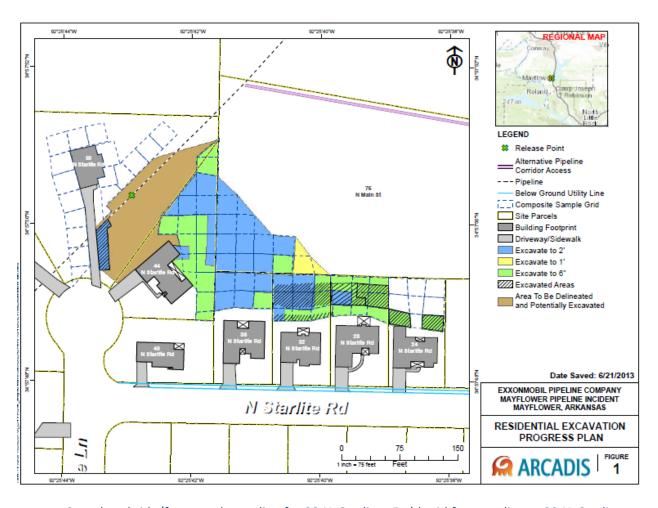

- Completed side/front yard sampling for 28 N. Starlite. Est'd grid for sampling at 32 N. Starlite.
- Performed excavation activities at 32 N. Starlite.
- Supported pot-holing and inspection of utilities east of 24 N. Starlite. No oil or sheen observed.
- Currently awaiting sampling results of additional potholing/excavation activity conducted at 24 and 50 N. Starlite.
