

ADEQ

ARKANSAS
Department of Environmental Quality

AFIN: _____ Permit No.: AR0042846

Date: _____ By: Byrum


Project: site visit notes

Sheet 1 of 1

Printed on recycled content paper
ADEQ Engineer/Geologist Seal Pad - revised 2002



- ⇒ SW2 to be permitted under IGP (active mining runoff)
COD, TSS, O₂G, pH
- SW1 - not disturbed
- 5300 tons/day cement production max allowable under air permit
- Copper sampled at outfall 002 at first discharge
- PPS required at outfall 001 at first discharge

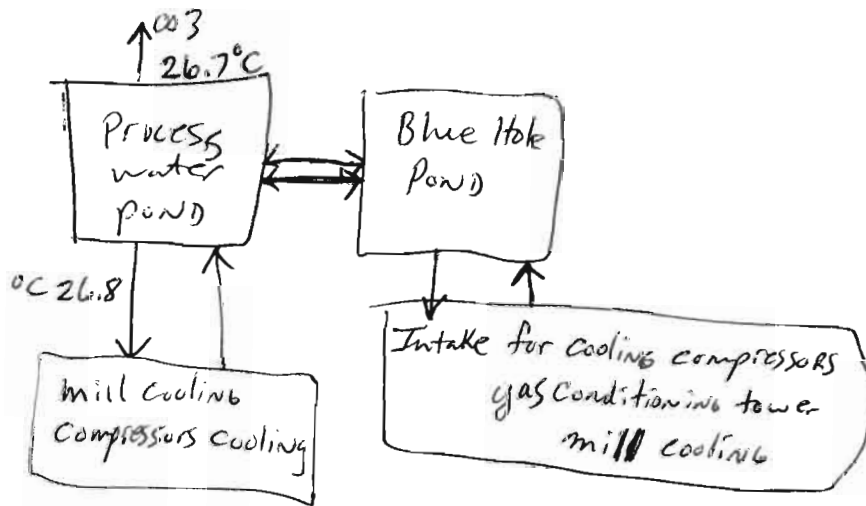

Temp ~~required~~

- intake screen at process water pond (permit will require Temp monitoring here)
- 1hr measure 003 + intake within 1 hour when 003 is discharging once/month
- ~~get~~ get wa-based numbers for BOD, NH₃, DO for 003.
